914 Bloomfield HB

Start date
4/20/26

Rip off
60 mil -
1/2” iso -

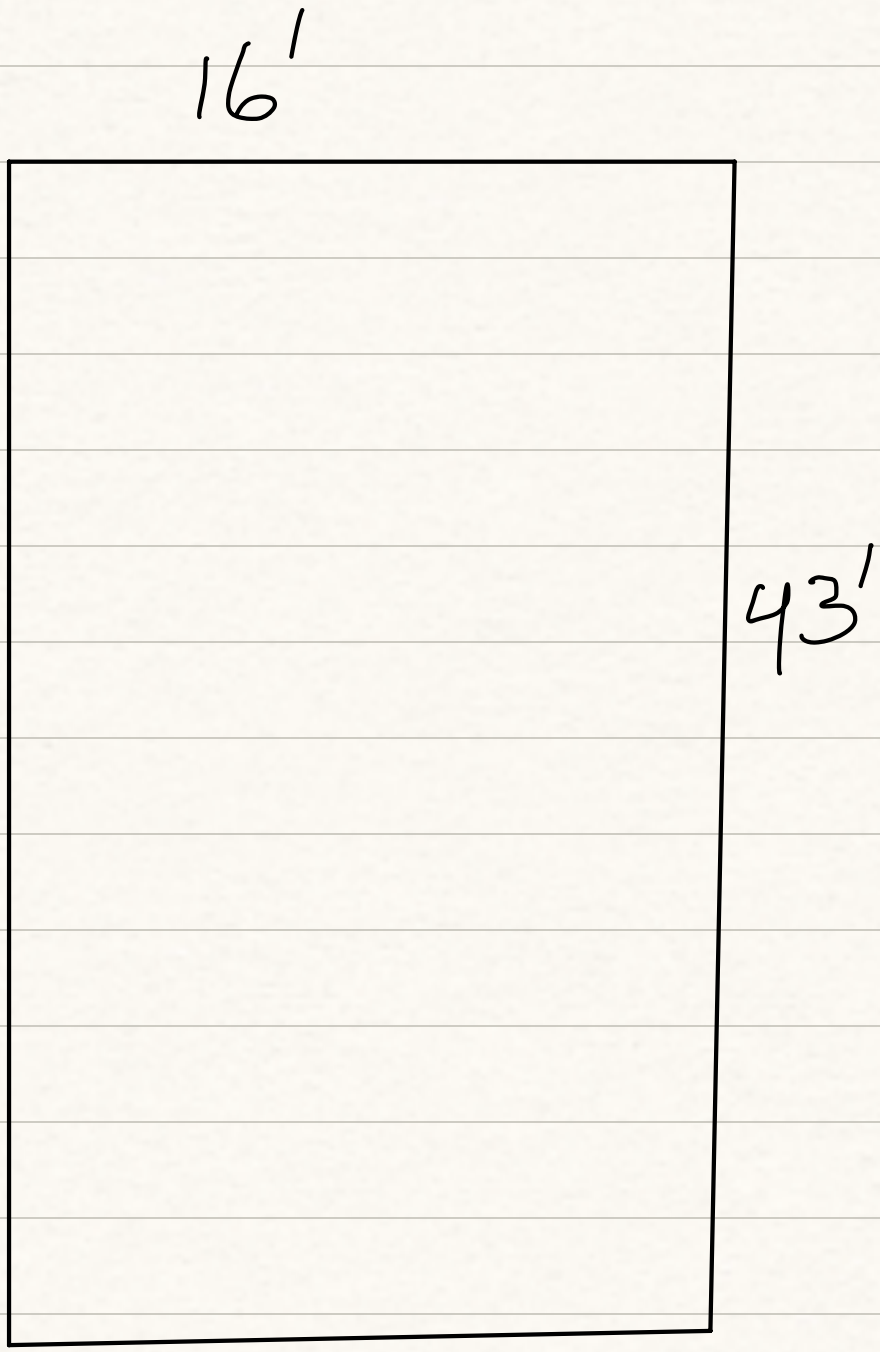

8 Blocks For Boom

18" Tapes x 8

Skylights
FCM2222 FCM 2230
FCM 3046

Wood Hatch
31 x 36

metal

DE 4"X4" - 5'
Sep 3X3 - 10'
Sep 4X4 - 40'
SM - 30'
GS4 - 53'
GS 6 - 20

Drain

Tube + Flange 3"
Commercl 3" + 4"

Wrap Ducts

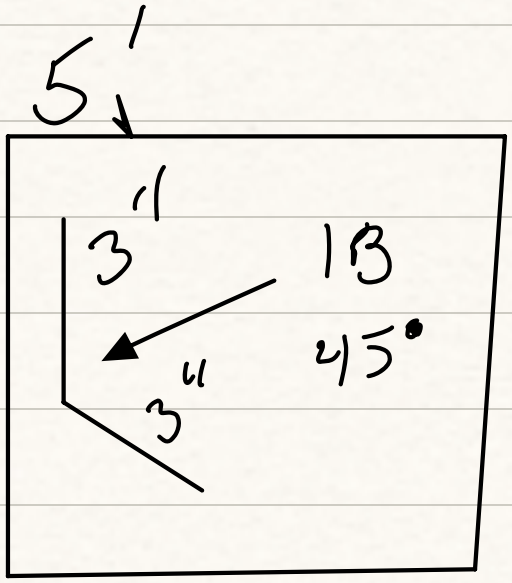

ISO

X - 4
IS Corners - 2
OS Corners 37

Wood

2X12 - 20'
2X8 - 40'
4X4 PS - 8'

PP metal 10'
1 x Pitch Pocket Filler

2x4 - 12' - 12'

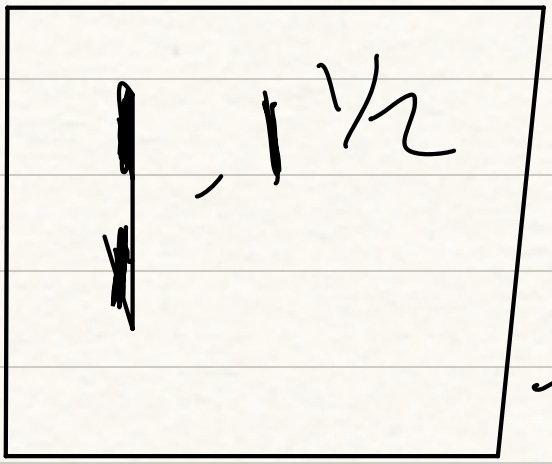

with
3 1/4" Items
For Term For ac unit

Get neighbor Know to move
Solar for Bell
914 Garden

---

electric outlet on Roof

Hvac disconnect

6" High wind Cap ?

Pipes

A - 3
B - 1
D - 1

WORK ORDER

Capitol Roofing Company
2 Getty Avenue
Clifton, NJ 07011
sej@capitolroofingco.com
(973) 414-0660

Job Address: 914 Bloomfield Street
Hoboken, NJ 07030

Salesman/Customer Rep
Eric Deribin
eric@capitolroofingco.com
(973) 414-0660

Job Id 2408-6025390-01	**Job Name** 914 Bloomfield St Hoboken	**Work Order Amount**	**$0.00**
Work Order # 0699	**Work Order Date** 01/06/2026		

#	Type	Name	(Price / Unit) x Qty	Line Total
1	ACTIVITY	Install New Main & Extension Roof	($0.00 / Units) x 0.00	$0.00

Description: 1. Remove existing roof down to wood decking.
2. If there is any rotted wood, there will be an additional fee of $130.00 per sheet for wood replacement.
3. Mechanically attach ½" high density iso on field of roof.
4. Mechanically attach and hot air weld white pvc roofing system. Mfg: IB Roof systems.
5. Replace pvc drains.
6. Reline built on gutter.
7. Price includes repitching front cornice to allow foreman to drain onto roof.
8. Supply and install new wood hatch over existing opening.
9. Install new flashings around roof protrusions as needed.
10. Install pitch pockets as needed.
11. Install gravel stop on front, side, and rear roof edge with 6" cover strip welded.
12. Supply and install three (3) new fixed curb mounted (FCM) skylight units over existing openings. Mfg: Velux

Total **$0.00**

Note:

60 mil white - 19sq
1/2" Iso - 10sq
Skylights - FCM 2222, FCM 3046, FCM 2230
Labor - $7,050.00

extension

Price for 3 Hip Ridge Skylights

at the very least

Change the 3046 to

Hip Ridge
